
IT PROJECT MANAGEMENT · AGILE REPORT

Agile, the way we build Unveil

A dating web service where you meet the person first, built in six two-week sprints inside five stage gates.



We are in Sprint 3 of 6

Marlen Kalbayev · Diyor Khabibullayev · Yeldos Bakayev · Farkhad Amanbayev

Lecturer: Muhammad Khalil Shahid · Group presentation

Four values of the Agile Manifesto

01

Individuals and interactions

over processes and tools

Us: a weekly stand-up and a team chat instead of long status reports.

02

Working software

over comprehensive documentation

Us: every sprint ends with a demo that really runs.

03

Customer collaboration

over contract negotiation

Us: the lecturer and test users see every Sprint Review.

04

Responding to change

over following a plan

Us: MoSCoW lets us drop a “Could” instead of moving a date.

Agile Manifesto, 2001 · the items on the right still matter, we value the left more · plus 12 principles

Waterfall vs Agile on our project

Aspect	Waterfall: plan, then build	Agile: build in small steps (Unveil)
Planning	Whole project upfront	Gates fixed, next sprint planned in detail
Scope	Frozen in the charter	Product Backlog in MoSCoW order
Delivery	One release in week 14	A working increment every 2 weeks
Feedback	At the final demo	At every Sprint Review
Change	Formal change request	PO reorders the backlog; new scope needs sponsor OK
Progress	Earned value: SPI, CPI	Earned value + velocity and burndown

Will users wait 24 hours for a photo? Is a free AI good enough? With Waterfall we learn it in week 14, too late. With Agile, every two weeks.

A two-week loop and three roles

DAY 1

Sprint Planning

45 min. Pick the Sprint Goal and the stories.

DAILY + WEEKLY

Stand-up

Chat update every day, 15-min call weekly.

DAY 10

Sprint Review

30 min. Live demo, feedback from the lecturer.

DAY 10

Retrospective

20 min. One thing we change next sprint.

PRODUCT OWNER

Yeldos

Owns user stories, orders the backlog, talks to the sponsor.

SCRUM MASTER

Marlen

Runs the events, removes blockers, keeps WBS, CPM and risks.

DEVELOPERS · ALL FOUR

Diyor · API, matching
Farkhad · sign-up, tests, chat
Marlen · AI co-pilot
Yeldos · privacy, testing

Scrum: 3 roles, 5 events, 3 artifacts (Product Backlog, Sprint Backlog, Increment) · Source: The Scrum Guide, 2020

The backlog: user stories in MoSCoW order

#	As a user, I want to…	MoSCoW	SP	Sprint
1	Sign up and log in	**Must**	3	S3
2	Take personality and values tests	**Must**	8	S3
3	Get a match from the algorithm, no swipes	**Must**	13	S4
4	Chat with my match in real time	**Must**	8	S4
5	See their photo after 24 hours of chat	**Must**	5	S4
6	Edit my profile and see my test results	**Should**	5	S3
7	Play AI co-pilot games and questions in chat	**Should**	8	S5
8	Choose who sees my data (privacy settings)	**Should**	5	S5
9	Get an AI insight report after a week	**Could**	5	S6

60 story points (SP), sized by planning poker (1, 2, 3, 5, 8, 13) · Won’t have this term: swipes, mobile app, video calls, payments

Six sprints inside five stage gates

Wk 1–2 · Gate 1

Weeks 3–14 · six two-week Scrum sprints · 448 team-hours, $0

S1	S2	S3	S4	S5	S6
wk 3–4	**wk 5–6**	**wk 7–8**	**wk 9–10**	**wk 11–12**	**wk 13–14**
Requirements, user stories, WBS	Data model, API design, test design	Sign-up, onboarding tests, profiles	Matching, chat, 24-h reveal	AI co-pilot, privacy, testing	Insight report, fixes, final demo
		16 SP	**26 SP**	**13 SP**	**5 SP**
Gate 2 ✓	**✓ done**	**Gate 3 · now**	**Gate 4**	**Gate 5**	**Final demo**

Each gate is checked at a Sprint Review. Sprint 4 is the heaviest: it carries the critical path (G matching, I chat).

One board, one rule for “done”


TO DO	IN PROGRESS	DONE
Matching · Diyor	Sign-up, test UI · Farkhad	Charter · Marlen
Chat + reveal · Farkhad	Profiles, scoring · Diyor	User stories · Yeldos
Privacy · Yeldos	AI co-pilot · Marlen	Data model, API · Diyor

WIP limit 2 per person: finish before you start. **Pull** the next card from the top of To do. Board at week 7.

Definition of Done

- Reviewed, merged by PR
- Meets acceptance criteria
- Test accounts only
- Runs in the demo build
- Hours logged (for EVM)
- Board and backlog updated

What we track every sprint

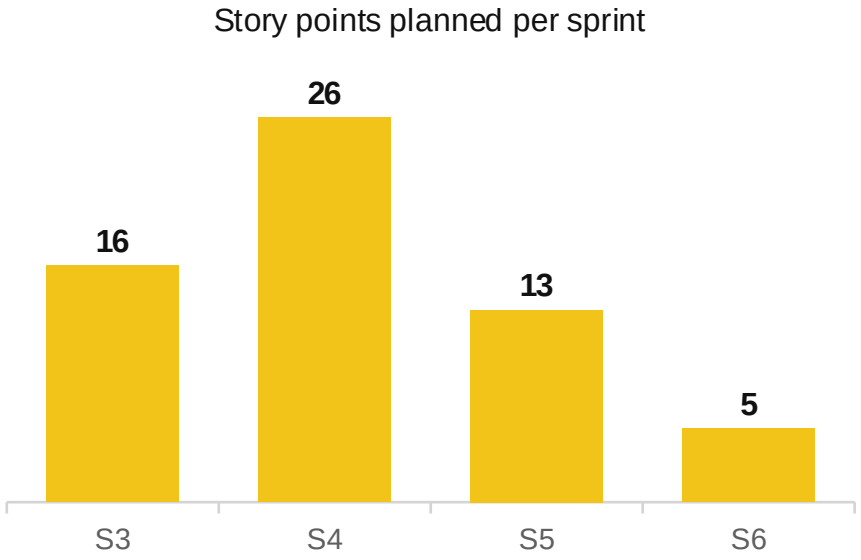

224 / 448 h

Team-hours used at week 7: exactly half

SPI 1.00 · CPI 1.00

Earned value stays our cost and time check

Alarm < 90%

If a sprint ends under 90% of planned points, the PO cuts a Could or Should

Sprint 4 holds 26 of 60 points. Fix: Marlen and Yeldos move from tasks with float (H, J) to help.

Keep the gates, run sprints inside them

Plan-driven tool we keep	Agile partner we add
Stage gates (wk 2, 4, 7, 10, 12)	Sprint Review where the gate is checked
WBS: all the work	Product Backlog of user stories
Critical path A → B → D → E → G → I → K → L	Sprint order: critical stories first
Earned value: SPI, CPI	Velocity and burndown
Risk register	Blockers at stand-up, lessons at the retro
Change control: sponsor approval	MoSCoW: the PO reorders inside the fixed scope

Time (14 weeks) and budget (448 h, $0) stay fixed. What we build can change inside them.

Agile has costs too, each with a fix

Risk (score from register)	Our Agile response
Team overload, exams (16, High)	Plan capacity per sprint; core features before exams; WIP limit 2
Scope creep (15, High)	Won’t list; new ideas go to the bottom of the backlog
Privacy of photos and tests (10)	In the Definition of Done: test accounts only, photo locked 24 h
AI quality and cost (9)	Prototype with mock prompts in S3; AI co-pilot stays a Should
Estimates are new to us	Planning poker; compare estimate and actual at every retro

Benefit: the sponsor and test users see a working part of Unveil every two weeks.

Sprint 4: the heart of Unveil

WEEK 9 · PLANNING

Goal: two test users get matched, chat, and see the photo after 24 hours

SPRINT BACKLOG

Matching (13) + chat (8) + 24-h reveal (5) = 26 SP

WEEK 10 · REVIEW

Live demo at Gate 4, then the retrospective

Questions?
